


Aperi IDVT - Phase 3

Week Ending	02/02/07	02/09/07	02/16/07	02/23/07	03/02/07	03/09/07	03/16/07	03/23/07	03/30/07	04/06/07	04/13/07	04/20/07	04/27/07
Planned Exposed	25	50	50	50	75	100	125	150	175	190	200	200	200
Planned Successful	24	48	48	48	70	92	116	140	164	178	182	182	192
Actual Exposed	22	45	45	45	84	0	0	0	0	0	0	0	0
Actual Successful	21	43	43	43	78	0	0	0	0	0	0	0	0
Blocked	0	0	0	0	0	0	0	0	0	0	0	0	0


Plan % Exposed	13%	25%	25%	25%	38%	50%	63%	75%	88%	95%	100%	100%	100%
Plan % Success	12%	24%	24%	24%	35%	46%	58%	70%	82%	89%	91%	91%	96%
Actual % Exposed	11%	23%	23%	23%	42%	0%	0%	0%	0%	0%	0%	0%	0%
Actual % Success	11%	22%	22%	22%	39%	0%	0%	0%	0%	0%	0%	0%	0%
% Blocked	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%

Aperi IDVT (Phase 3)
(Preliminary scenario count subject to change)

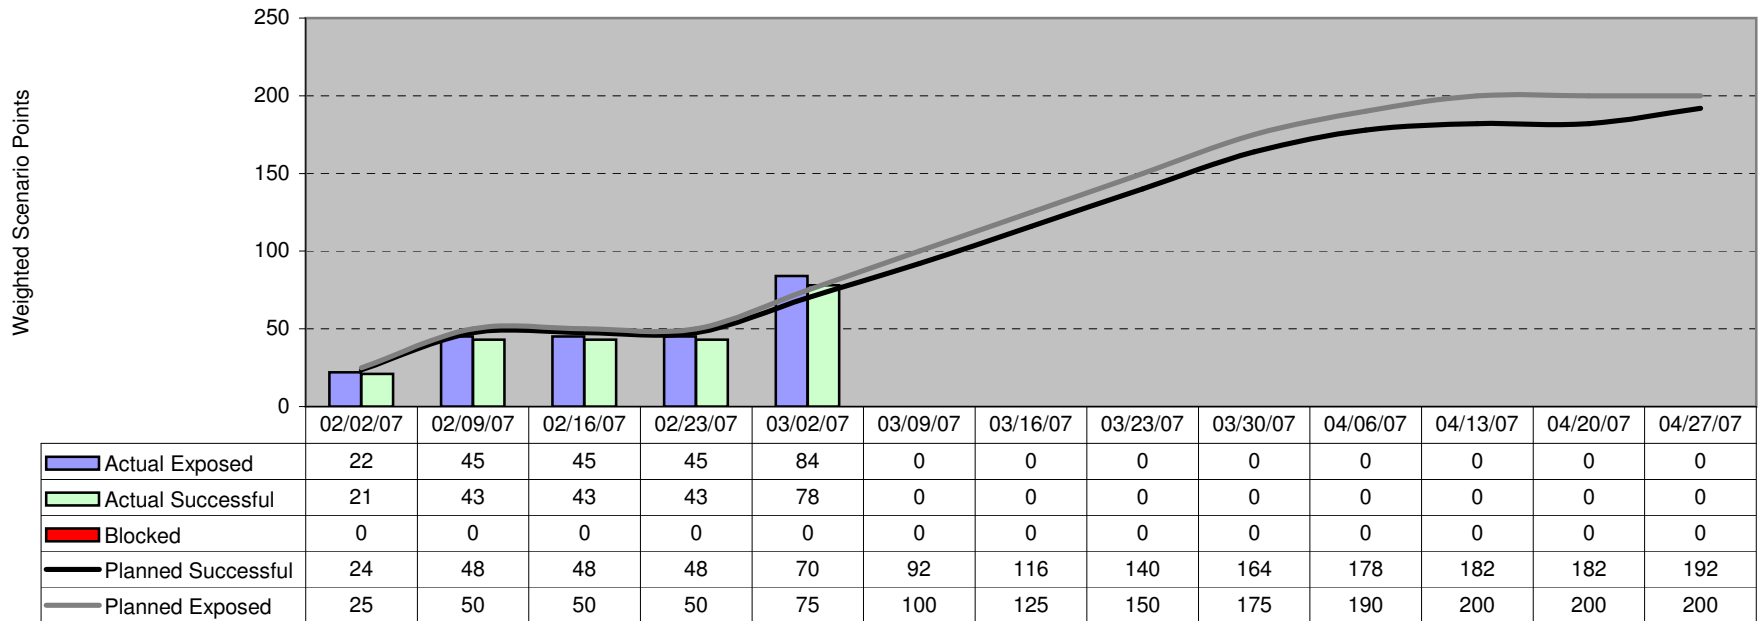

Aperi IDVT, Phase 3 Defect Discovery Week Ending	02/02/07	02/09/07	02/16/07	02/23/07	03/02/07	03/09/07	03/16/07	03/23/07	03/30/07	04/06/07	04/13/07	04/20/07	04/27/07
IDVT Estimate													
New (open)	29	29	29	29	31	0	0	0	0	0	0	0	0
Assigned (working)	3	3	3	3	3	0	0	0	0	0	0	0	0
Resolved (verified)	0	0	0	0	4	0	0	0	0	0	0	0	0
Verified (closed)	0	0	0	0	2	0	0	0	0	0	0	0	0
Reopened	0	0	0	0	1	0	0	0	0	0	0	0	0
Invalid	0	0	0	0	1	0	0	0	0	0	0	0	0
Canceled	0	0	0	0	0	0	0	0	0	0	0	0	0
Total (N.I. can/inv)	32	32	32	32	41	0	0	0	0	0	0	0	0


Aperi IDVT (Phase 3) Defect Discovery
(Cancel/Return not in total)

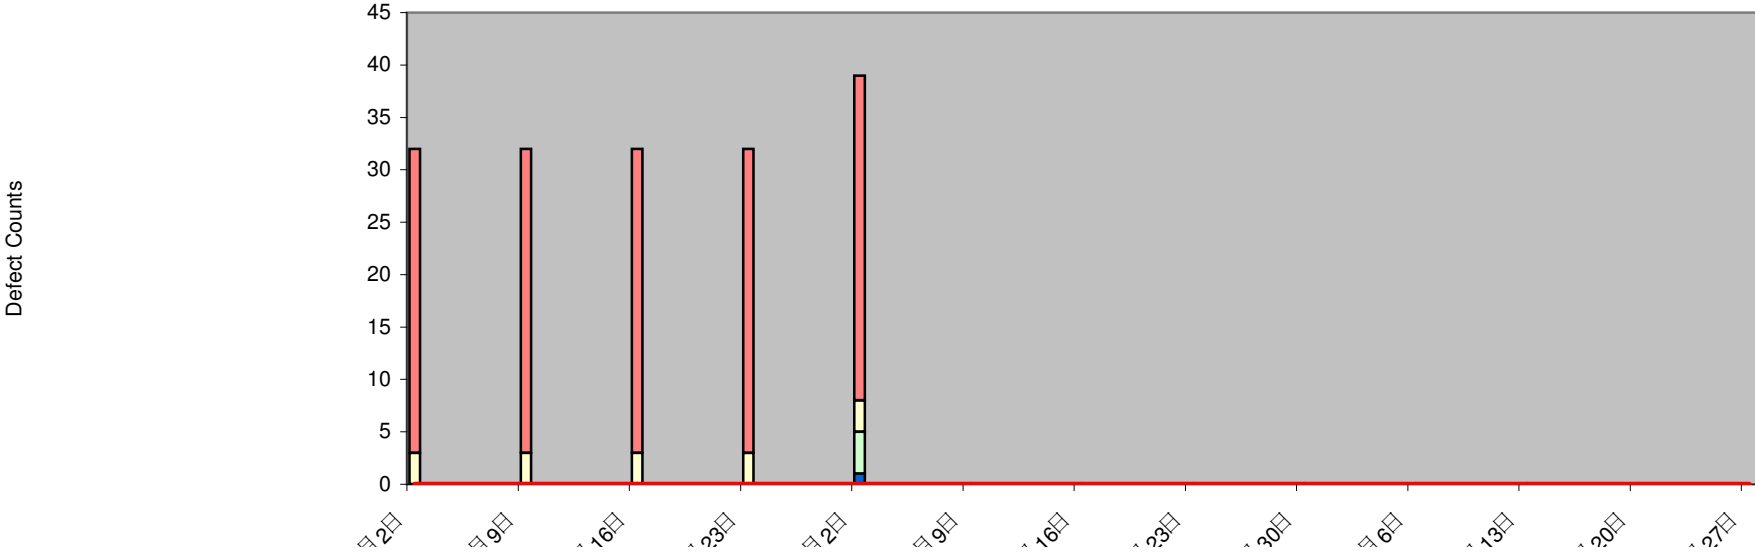

	02/02/07	02/09/07	02/16/07	02/23/07	03/02/07	03/09/07	03/16/07	03/23/07	03/30/07	04/06/07	04/13/07	04/20/07	04/27/07
New (open)	29	29	29	29	31	0	0	0	0	0	0	0	0
Assigned (working)	3	3	3	3	3	0	0	0	0	0	0	0	0
Resolved (verified)	0	0	0	0	4	0	0	0	0	0	0	0	0
Reopened	0	0	0	0	1	0	0	0	0	0	0	0	0
Canceled	0	0	0	0	0	0	0	0	0	0	0	0	0
IDVT Estimate													

Defect Inventory: Sev 1,2	02/02/07	02/09/07	02/16/07	02/23/07	03/02/07	03/09/07	03/16/07	03/23/07	03/30/07	04/06/07	04/13/07	04/20/07	04/27/07
New (open)	0	0	0	0	1	0	0	0	0	0	0	0	0
Assigned (working)	0	0	0	0	0	0	0	0	0	0	0	0	0
Total	0	0	0	0	1	0	0	0	0	0	0	0	0

Aperi (Phase 3) IDVT Defect Inventory
Severity 1 (blk,cri) and 2 (maj)
Open/Working States




	2006年11月10日	2006年11月13日	2006年11月16日	2006年11月19日	2006年11月22日	2006年11月25日	2006年11月28日	2006年12月1日	2006年12月4日	2006年12月7日	2006年12月10日	2006年12月13日	2006年12月16日	2006年12月19日	2006年12月22日
	02/02/07	02/09/07	02/16/07	02/23/07	03/02/07	03/09/07	03/16/07	03/23/07	03/30/07	04/06/07	04/13/07	04/20/07	04/27/07		
■ New (open)	0	0	0	0	1	0	0	0	0	0	0	0	0	0	0
■ Assigned (working)	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0

Defect Discovery

<u>Defects</u>	<u>Severity</u>	<u>Description</u>
0	1	<i>Blocker, Critical</i>
1	2	<i>Major</i>
34	3	<i>Normal</i>
0	4	<i>or, Trivial, Enhancen</i>

Aperi IDVT (Phase 3)
 IDVT Defect Discovery By Severity
 (Not including canceled and invalid)

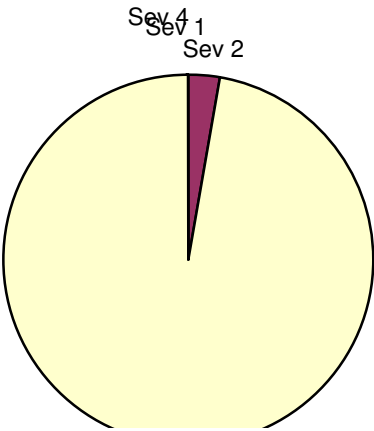



Sev 3

1

」

」

]

]

